


Hi Melanie,

Please put this on the website.  
There is a link on the ~~the~~  
Project information page 12-

Thanks  
Celin

**PROJECT 430(16) MED-42-17.80  
MAJOR RECONSTRUCTION  
PARTNERING RE-CONNECT  
FEBRUARY 28, 2017**




---

---

---

---

---

---

---

---

**AGENDA**

- I. Welcome
- II. Review of Charter and 10/11/16 Action Items
- III. Project Successes and Issues Pending Resolution
- IV. Project Schedule & Phasing
- V. Open Discussion and Action Item Review
- VI. Adjourn

---

---

---



---

---


---

---

---

**CHARTER REVIEW  
GOAL ASSESSMENT  
ACTION ITEM UPDATE**




---

---

---

---

---

---

---

---

## GOAL ASSESSMENT

- How are we meeting our goals?
- What action needs to be taken to address goals that are not being met?




---

---

---

---

---

---

---

---

## PROJECT GOALS

Goal	Performance to Date
Maintain a safe project site	<input checked="" type="checkbox"/>
Maximize public value and Contractor profitability	<input checked="" type="checkbox"/>
Build the project on time	<input checked="" type="checkbox"/>
Build the project within budget	<input checked="" type="checkbox"/> Change orders: Speedway, Marcum property settlements and a part code issue regarding waterline items on Reagan Parkway
Minimize inconvenience to the traveling public	<input checked="" type="checkbox"/>
Minimize inconvenience to the business community	<input checked="" type="checkbox"/>
Maintain emergency services access	<input checked="" type="checkbox"/>
Develop a work environment that promotes mutual respect	<input checked="" type="checkbox"/>

---

---

---

---

---

---

---

---

## COMMUNICATION GOALS

Goal	Performance to Date
Identify and follow the chain of command for all communication	<input checked="" type="checkbox"/>
Establish and maintain honest and open communication	<input checked="" type="checkbox"/>
Respond in a timely manner to all project issues	<input checked="" type="checkbox"/>
Regular, accurate communication with the City of Medina and local businesses	<input checked="" type="checkbox"/>
Complete, clear, and concise correspondence	<input checked="" type="checkbox"/>
Electronic file of the project	<input checked="" type="checkbox"/>

---

---

---

---

---

---

---

---

### PROBLEM SOLVING GOALS

Goal	Performance to Date
Identify and address all problems as soon as possible	☒
Resolve problems at the lowest level when possible	☒
Communicate, implement, and document solutions	☒
Seek solutions, not blame	☒
Involve tradesmen in the solutions whenever possible	☒
Follow the designated chain of command	☒
Follow the Dispute Resolution Process	☒
Maintain a "Best for the Project" approach	☒

---

---

---

---

---

---

---

---

---

---



### 10/11/16 PARTNERING MEETING ACTION ITEMS UPDATE




---

---

---

---

---

---

---

---

---

---

### ACTION ITEMS

- There were eight action items from the 10/11/16 partnering meeting:
  1. Progress meeting invitations
  2. Utilities
  3. Concrete median islands
  4. Business communication planning
  5. Business concerns
  6. Property owners
  7. Emergency service notification protocol
  8. Traffic signal meeting

---

---

---

---

---

---

---

---

---

---

**PROGRESS MEETINGS**

- All pertinent parties were identified and have been invited to each progress meeting.

---

---

---

---

---

---

---

---

**UTILITIES**

- The ODOT Project Engineer and the Medina City Engineer confirmed the utility contact information is correct.
- DiGioia identified the size of the area that needed to be marked out.

---

---

---

---

---

---

---

---

**CONCRETE MEDIAN ISLANDS**

- Letter was sent to Medina Township on 2/22/17.
- Based upon safety and aesthetic considerations, the concrete medians will remain.

---

---

---

---

---

---

---

---

**BUSINESS COMMUNICATION  
PLANNING**

- The first Business Meeting/Open House will be held this afternoon from 4:00 p.m. – 6:00 p.m.
- Other events will be held for each season, if circumstances require it.
- Media contacts were provided.
- News stories have been and will be developed.
- A weekly update is sent to the media.
- A project-specific website has been created.

 [http://www.dot.state.oh.us/districts/D03/Pages/MED-42\\_WideningProject.aspx](http://www.dot.state.oh.us/districts/D03/Pages/MED-42_WideningProject.aspx)

---

---

---

---

---

---

---

---

**BUSINESS CONCERNS**

- Waterline tie-ins will be done at night. Waiting to have a known phased schedule before providing information to the specific businesses.

---

---

---

---

---

---

---

---

**PROPERTY OWNERS**

- ODOT provided a list to the Contractor of property owners who had not settled.

---

---

---

---

---

---

---

---

**EMERGENCY SERVICE  
NOTIFICATION PROTOCOL**

- ODOT and the City established an emergency service notification protocol. Dan Gladish from the City is a main contact.

---

---

---

---

---

---

---

---

**TRAFFIC SIGNAL MEETING**

- The Project Team and the City met to discuss traffic signal activation issues.

---

---

---

---

---

---

---

---

**PROJECT SUCCESSES AND  
PENDING ISSUES**



---

---

---

---

---

---

---

---

### **PROJECT SUCCESSES**

- The Project has worked very well together to keep the job moving forward.
- Significant re-phasing was developed to keep the project on track to meet the 10/15/18 completion date.
- Drainage work was performed during the winter to shorten the duration of the mainline widening work.
- Left-turn lanes included to minimize inconvenience to the traveling public.

---

---

---

---

---

---

---

---

### **PENDING ISSUES**

- Fine-tuning the Project's re-phasing to address the utility impacts.

---

---

---

---

---

---

---

---

### **PROJECT 430(16) MED-42-17.80 SCHEDULE AND PHASING**



---

---

---

---


---

---

---

---



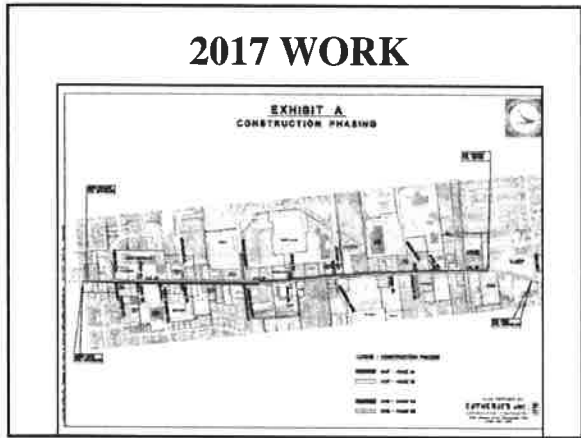


---

---

---

---

---

---

---

---

- Work will begin the week of March 13, 2017.
- Critical items:
  - Work needs to be done for the season by November 1<sup>st</sup>.
  - All of US 42 north of Reagan Parkway will be completed, including intersections.
  - Pavement has been added to provide left-turn lane movements during construction.
  - Sidewalk and driveway work may be on-going.
- Two primary phases, from the public's perspective:
  - March - July
  - July - October

---

---

---

---

---

---

---

---

- March - July:
  - Beginning 3/13/17, build the west side of US 42, north of Reagan Parkway, heading southbound.
  - Work on Grande Blvd. will begin the week of 3/13/17.
  - Hillview Rd. closure will begin in May and last for 30 days.

---

---

---

---

---

---

---

---

• July – October:

- Mid-July, traffic will flip to build the east side of US 42, north of Reagan Parkway, heading northbound.
- Stonegate Rd. closure will begin in early August.
- Ledgewood Road closure will happen in September.

---

---

---

---

---

---

---

---

• Frontier will be out there to clear their utilities and will not leave until their work is finished.

- They will work north of Reagan Parkway, then work south of Reagan Parkway to finish.
- The reconstruction of Reagan Parkway will depend upon the Frontier relocation work.
  - If Frontier is out of the way in time for Reagan to be built in 2017, it will. The west side will be re-built, then the east side.
  - If Frontier is not out of the way, then Reagan Parkway will be built in 2018, beginning with the east side, then the west side.

---

---

---

---


---

---

---

---

## 2018 WORK

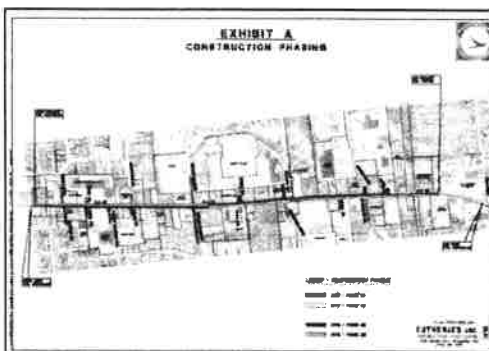

---

---

---

---

---

---

---

---

- Build US 42, south of Reagan Parkway, starting with the east side, then completing the west side of the road.
- Concrete islands.
- Surface course.
- Permanent traffic signals.
- Lighting.
- Final pavement markings.

---

---

---

---

---

---

---

---



**OPEN DISCUSSION & PARTNERING FOLLOW-UP**



---

---

---

---

---

---

---

---

- Any other issues that need to be addressed?
- Any questions?
- Any concerns?

---

---

---

---

---

---

---

---

- Partnering follow-up:
  - Action Plan Review
  - Re-connect session to be scheduled at the end of the 2017 season to debrief how it went and to review work to be done during the winter.
  - Re-connect session to be scheduled early spring 2018 to discuss work to be done that season.

---

---

---

---

---

---

---



**ADJOURN  
THANK YOU!**



---

---


---

---

---

---

---

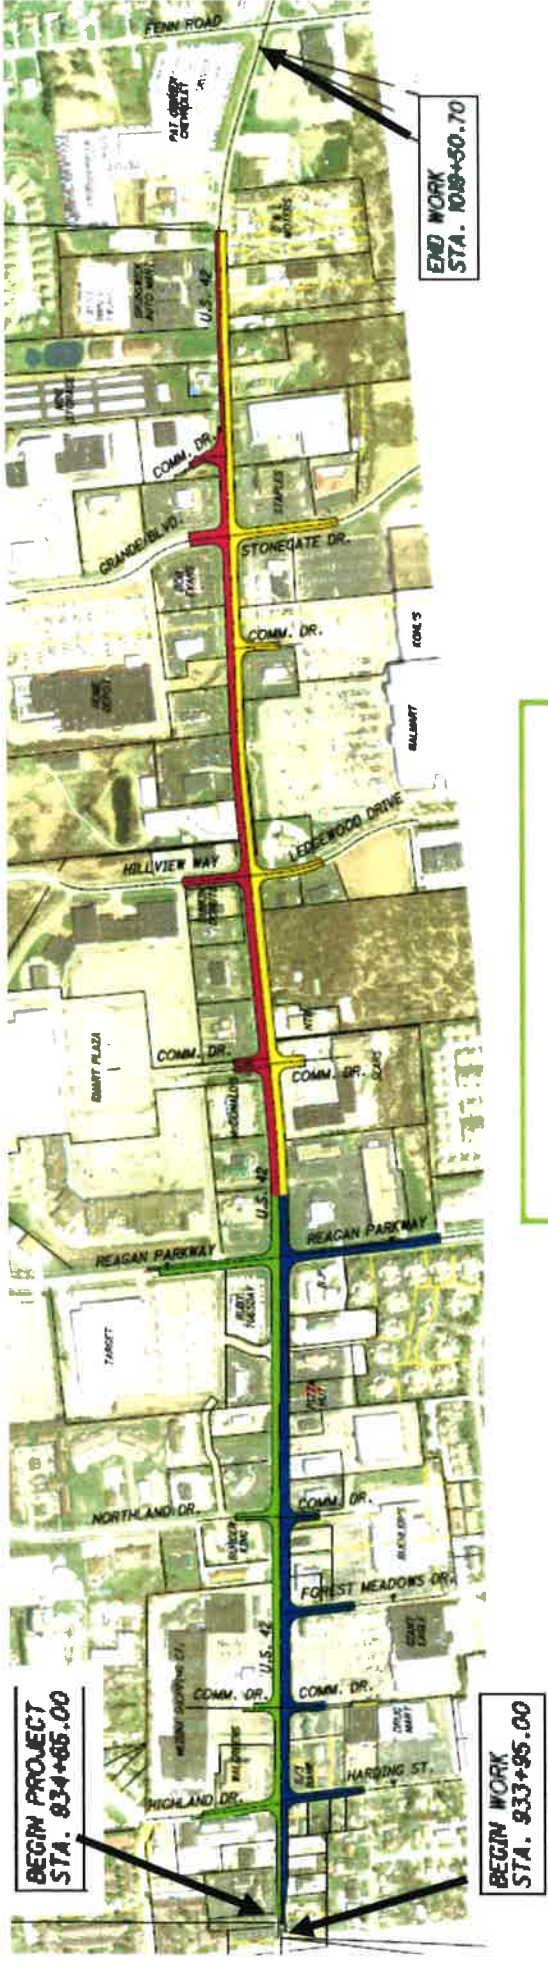

**Beginning: March-July**

All of US 42, north of Reagan Parkway, will be completed- including intersections


Pavement has been added to provide left-turn lane movements during construction

Two primary phases: March-July & July-October

Beginning in March, building the west side of US 42, north of Reagan Parkway, heading southbound

Work on Grand Blvd. will begin

Hillview Rd. closure will begin in May and last around 30 days.

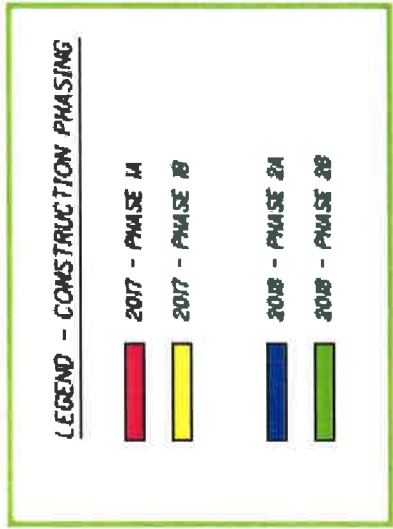

**July-October**

Beginning in July traffic will flip to build the east side of US 42, north of Reagan Parkway, heading northbound

Stonegate Rd. closure will begin in early August

Ledgewood Rd. closure will happen in September

**Reagan Parkway**

The reconstruction of Reagan Parkway will depend upon the utility relocation work

If utilities are relocated in time, work on Reagan Parkway will be done in 2017

However, if utilities are NOT relocated in time then work on Reagan Parkway will be done in 2018





MED-42-17.80 1



# EXHIBIT A CONSTRUCTION PHASING



LEGEND - CONSTRUCTION PHASING

- 2017 - PHASE 1A
- 2017 - PHASE 1B
- 2018 - PHASE 2A
- 2018 - PHASE 2B

PLAN PREPARED BY:  
**EUTHEMIS INC.**  
 CONSULTING ENGINEERS  
 8225 Montgomery Drive, Cincinnati, Ohio  
 (440) 260-1555

BEGIN PROJECT  
 STA. 834+65.00

BEGIN WORK  
 STA. 833+95.00

END PROJECT  
 STA. 807+50

END WORK  
 STA. 809+90.70

The project includes the following improvements:

Reconstruction and widening to provide two thru lanes and left turn lanes at the side road intersections

Raised median and a center two-way left turn lane in Medina Township

10' wide multi-use path (west side) & 5' wide walk (east side)

New roadway lighting within the raised median

Addition of curb and gutter with new storm sewers

New water main within the City of Medina

New concrete driveway aprons

New traffic signals at 8 intersections

Management of access along US Route 42 corridor

## PROJECT INFORMATION

For more information & to be added to our weekly update visit

<http://www.transportation.ohio.gov/42>

### Email List Sign Up

If you would like news from ODOT on this project, join our mailing list! Provide your email address and hit the Sign Up button.

Email address:

Your name:

# US 42 Widening Project



## Major Reconstruction

Start Construction: Fall 2016

End Construction: October 2018

## Business Meeting

2017 Season

Question or concerns call the Public Information Office at 419-207-7181 or 419-207-7182



Page 12
